

Dosing area

- Completed all concrete roadway
- Footpaths substantially completed
- Tanks filled with potable water in readiness for Aquazone to complete their hydrostatic testing

Tertiary Treatment Area

- Slab fully complete to the backwash pumping station
- All DI pipe works completed
- Commenced with the concrete roadway slabs, 50% completed
- Footway substantially completed

Site Wide Ducting

- Electrical install 96% completed
- Above ground pipe work completed
- Rising mains pressure tested and passed off
- All Gravity drainage air tested and passed off
- Tip area civilised and top soiled along with areas around the tertiary treatment area and dosing areas
- Potable water supply installed

MCC

- New MCC powered up during the period in readiness for commissioning works to commence.

Existing Tertiary PS

- Installed over pumping to bypass the PS
- Commenced with pump change over

Dosing area concrete slab



Tertiary Treatment Slab commencing




Above Ground Pipework



Walkway + Mowing strip



Electrical Install

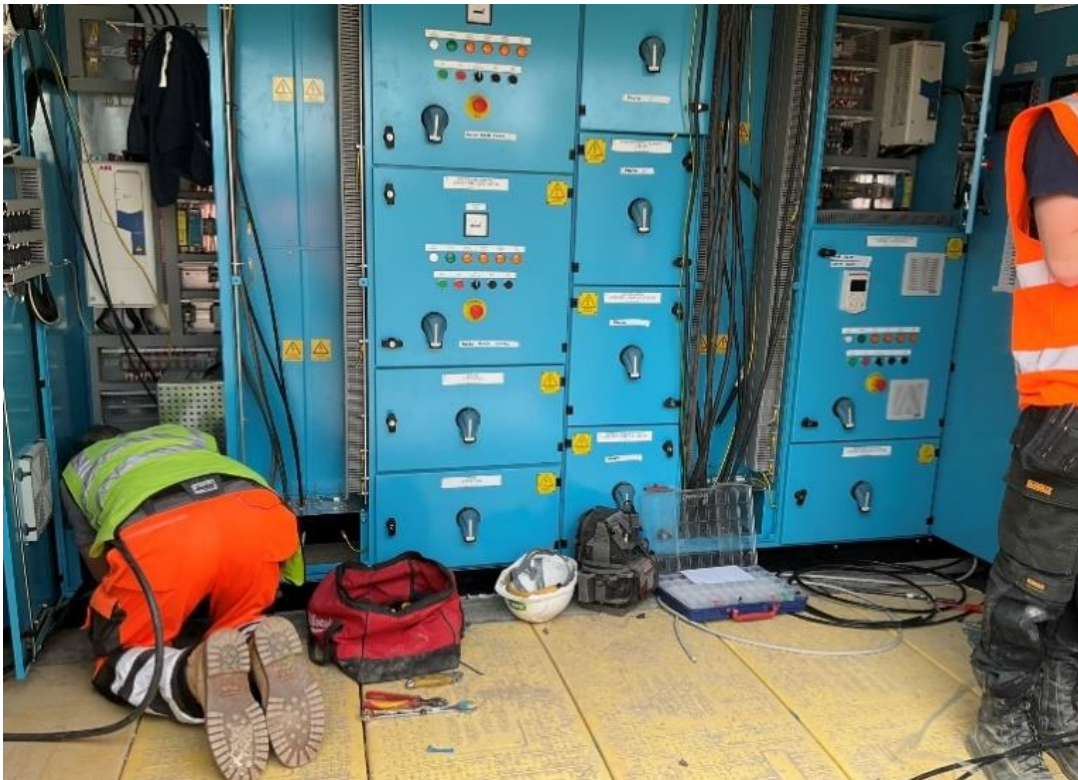



Tertiary Treatment Pipe



Activities Planned for next month.

Tertiary PS

Pump Change over and then commissioning the new pumps to allow us to remove the over pumping.

Dosing area

- Aquazone to complete their commissioning works Oct 2024

Tertiary Treatment Area

- Complete the concrete roadways
- Hydroc to commission the Mecana unit
- Commission the new Tertiary treatment plant 09 Oct 2024.

Site Wide

- GT Commissioning engineer to commence with Commissioning works

MCC

- Chequer plate to floor

Back Wash Pumping station delivered to site

Activities Planned for next month.

- Install Backwash pumping station
- Electrical works to connect the HSAF units
- Test the HSAF units
- Install the over pumping and pumps and Tanks
